

# Work Order ID 61768



Page 1

Thursday, September 02, 2010 11:28:13 AM

Item ID: D350-748-201

Accept



Setup Start



Revision ID:

Stop



Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010 Start Qty: 1.00



Cust Item ID:

Required Date: 9/20/2010 Req'd Qty: 1.00

Customer:

Reference:

Approvals:

Process Plan:

*[Signature]*

Date: 10-9-02

Tooling:

Date:

Run Start



QC:

Date:

SPC (Y/N):

Date:

Stop



Sequence ID/  
Work Center ID

Operation  
Description

Set Up/  
Run Hours

Tool ID

Tool #

Plan  
Code

Accept  
Qty

Reject  
Qty

Reject  
Number

Insp.  
Stamp

Draw Nbr

Revision Nbr

D350-748-241

Rev E

100

0.00



DOCUMENT CONTROL

DC

Memo

0.00

Document Control

Photocopy bluefile & type labels per PPPD350-748-201

CHG001

*8/10/2010*

*DP* *for CL 11-02-03*  
*10-12-7*

110

0.00



BENDING MACHINE - CROSSTUBES

CNC Bend 2

Memo

0.00

CNC Alpha 160 Bender

Bend tube as per Dwg D350-748-241 using CNC bender program D350A and Folio FT

*DP* *10-12-7*

120

QC15- Crosstube Dimensional Check

0.00



QC

Memo

0.00

Quality Control

*8/10/2010*

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

\_\_\_\_\_

Thursday, September 02, 2010 11:28:13 AM

**Accept**

1  
 2  
 3  
 4  
 5  
 6  
 7  
 8  
 9  
 10  
 11  
 12  
 13  
 14  
 15  
 16  
 17  
 18  
 19  
 20  
 21  
 22  
 23  
 24  
 25  
 26  
 27  
 28  
 29  
 30  
 31  
 32  
 33  
 34  
 35  
 36  
 37  
 38  
 39  
 40  
 41  
 42  
 43  
 44  
 45  
 46  
 47  
 48  
 49  
 50  
 51  
 52  
 53  
 54  
 55  
 56  
 57  
 58  
 59  
 60  
 61  
 62  
 63  
 64  
 65  
 66  
 67  
 68  
 69  
 70  
 71  
 72  
 73  
 74  
 75  
 76  
 77  
 78  
 79  
 80  
 81  
 82  
 83  
 84  
 85  
 86  
 87  
 88  
 89  
 90  
 91  
 92  
 93  
 94  
 95  
 96  
 97  
 98  
 99  
 100  
 101  
 102  
 103  
 104  
 105  
 106  
 107  
 108  
 109  
 110  
 111  
 112  
 113  
 114  
 115  
 116  
 117  
 118  
 119  
 120  
 121  
 122  
 123  
 124  
 125  
 126  
 127  
 128  
 129  
 130  
 131  
 132  
 133  
 134  
 135  
 136  
 137  
 138  
 139  
 140  
 141  
 142  
 143  
 144  
 145  
 146  
 147  
 148  
 149  
 150  
 151  
 152  
 153  
 154  
 155  
 156  
 157  
 158  
 159  
 160  
 161  
 162  
 163  
 164  
 165  
 166  
 167  
 168  
 169  
 170  
 171  
 172  
 173  
 174  
 175  
 176  
 177  
 178  
 179  
 180  
 181  
 182  
 183  
 184  
 185  
 186  
 187  
 188  
 189  
 190  
 191  
 192  
 193  
 194  
 195  
 196  
 197  
 198  
 199  
 200  
 201  
 202  
 203  
 204  
 205  
 206  
 207  
 208  
 209  
 210  
 211  
 212  
 213  
 214  
 215  
 216  
 217  
 218  
 219  
 220  
 221  
 222  
 223  
 224  
 225  
 226  
 227  
 228  
 229  
 230  
 231  
 232  
 233  
 234  
 235  
 236  
 237  
 238  
 239  
 240  
 241  
 242  
 243  
 244  
 245  
 246  
 247  
 248  
 249  
 250  
 251  
 252  
 253  
 254  
 255  
 256  
 257  
 258  
 259  
 260  
 261  
 262  
 263  
 264  
 265  
 266  
 267  
 268  
 269  
 270  
 271  
 272  
 273  
 274  
 275  
 276  
 277  
 278  
 279  
 280  
 281  
 282  
 283  
 284  
 285  
 286  
 287  
 288  
 289  
 290  
 291  
 292  
 293  
 294  
 295  
 296  
 297  
 298  
 299  
 300  
 301  
 302  
 303  
 304  
 305  
 306  
 307  
 308  
 309  
 310  
 311  
 312  
 313  
 314  
 315  
 316  
 317  
 318  
 319  
 320  
 321  
 322  
 323  
 324  
 325  
 326  
 327  
 328  
 329  
 330  
 331  
 332  
 333  
 334  
 335  
 336  
 337  
 338  
 339  
 340  
 341  
 342  
 343  
 344  
 345  
 346  
 347  
 348  
 349  
 350  
 351  
 352  
 353  
 354  
 355  
 356  
 357  
 358  
 359  
 360  
 361  
 362  
 363  
 364  
 365  
 366  
 367  
 368  
 369  
 370  
 371  
 372  
 373  
 374  
 375  
 376  
 377  
 378  
 379  
 380  
 381  
 382  
 383  
 384  
 385  
 386  
 387  
 388  
 389  
 390  
 391  
 392  
 393  
 394  
 395  
 396  
 397  
 398  
 399  
 400  
 401  
 402  
 403  
 404  
 405  
 406  
 407  
 408  
 409  
 410  
 411  
 412  
 413  
 414  
 415  
 416  
 417  
 418  
 419  
 420  
 421  
 422  
 423  
 424  
 425  
 426  
 427  
 428  
 429  
 430  
 431  
 432  
 433  
 434  
 435  
 436  
 437  
 438  
 439  
 440  
 441  
 442  
 443  
 444  
 445  
 446  
 447  
 448  
 449  
 450  
 451  
 452  
 453  
 454  
 455  
 456  
 457  
 458  
 459  
 460  
 461  
 462  
 463  
 464  
 465  
 466  
 467  
 468  
 469  
 470  
 471  
 472  
 473  
 474  
 475  
 476  
 477  
 478  
 479  
 480  
 481  
 482  
 483  
 484  
 485  
 486  
 487  
 488  
 489  
 490  
 491  
 492  
 493  
 494  
 495  
 496  
 497  
 498  
 499  
 500  
 501  
 502  
 503  
 504  
 505  
 506  
 507  
 508  
 509  
 510  
 511  
 512  
 513  
 514  
 515  
 516  
 517  
 518  
 519  
 520  
 521  
 522  
 523  
 524  
 525

**Setup Start**

\_\_\_\_\_

**Stop**

[illegible]

**Start Date:** 9/2/2010      **Start Qty:** 1.00

**Cust Item ID:**

**Required Date:** 9/20/2010      **Req'd Qty:** 1.00

**Customer:**

**Reference:**

Run Start

**Abstract**

**Approvals:**      **Process Plan:** \_\_\_\_\_ **Date:** \_\_\_\_\_ **Tooling:** \_\_\_\_\_ **Date:** \_\_\_\_\_

**Stop**

1101

QC: \_\_\_\_\_ Date: \_\_\_\_\_ SPC (Y/N): \_\_\_\_\_ Date: \_\_\_\_\_

### Operation Description

### Set Up/ Run Hours

## Tool ID

**Tool #****Plan  
Code**

**Accept  
Qty**

Reject  
Qty

### Reject Number

**Insp.  
Stamp**

125

0.00

[illegible]

HandFXtube

## Hand Finishing Crosstubes

## Memo

0.00

\*\*\*Stress relief\*\*\*

Heat treat crosstube as per QSI010 4.3

Start time 2h00

End time 6h00

SAD 10-12-68

127

QC5- Inspect part completeness to step on W/O

0.00

**00000000000000000000**

QC

## Quality Control

## Memo

0.00

Re means see second  
BAZ sheet

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

# Work Order ID 61768

Thursday, September 02, 2010 11:28:13 AM

Page 3

Item ID: D350-748-201

Accept

Setup Start

Revision ID:

Stop

Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010 Start Qty: 1.00

Cust Item ID:

Required Date: 9/20/2010 Req'd Qty: 1.00

Customer:

Reference:

Approvals: Process Plan: Date: Tooling: Date:

Run Start

QC: Date: SPC (Y/N): Date:

Stop

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

130

0.00



Crosstubes

Crosstubes

Memo

0.00

Crosstubes

1-Drill Tube as per Dwg D350-748-241 Using DT8876 Drill Jigs,  
Set-up drill table as per QS1 010

2-Deburr.

3-Engrave Part # and Batch # as per Dwg D350-748-241

4-Remove all marks from tube within limits of D350-748-241

5- Apply a light coat of LPS3 on the interior of tube

Batch: 109956

SAD 10-12-22

140

QC6- Inspect dimensions to drawing

0.00



QC

Memo

0.00

Quality Control

140.5

DEFLECT GEAR

10/12/21

issue R/O acumen for NDT

R/O: 13181

CL 10/12/21

rec'd + inspect attached report NDT to W/O

10/14/21

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

# Work Order ID 61768

Thursday, September 02, 2010 11:28:13 AM

Page 4

Item ID: D350-748-201

Accept

Setup Start

Revision ID:

Stop

Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010 Start Qty: 1.00

Cust Item ID:

Required Date: 9/20/2010 Req'd Qty: 1.00

Customer:

Reference:

Approvals: Process Plan: \_\_\_\_\_ Date: \_\_\_\_\_ Tooling: \_\_\_\_\_ Date: \_\_\_\_\_  
QC: \_\_\_\_\_ Date: \_\_\_\_\_ SPC (Y/N): \_\_\_\_\_ Date: \_\_\_\_\_

Run Start

Stop

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150 Outsource3 Outsource process - Cad plate	Outsource process-Cadplate per QSI017 4.1.9.1  Memo Issue P/O: <u>13/89</u> Stress relief at 375° for 5 hours Magnetic Particle Inspect per ASTM E1444 Cadium Plate per AMS-QQ-P-416B, Class 1, Type 2 Embrittle relief at 375° for 8 hours, Chromate Treat Possible Supplier: Southwest United Industries Ensure Certificate of Conformity is attached	0.00  0.00							<u>C2 10/12/22 (1)</u>
160 Packaging Packaging	Receive & Inspect for Damage & Mat'l Certs  Memo Ensure certificate of conformity is attached	0.00  0.00							<u>11/4/12 (1)</u>
170 QC Quality Control	QC5- Inspect part completeness to step on W/O  Memo	0.00  0.00							<u>8 up/24</u> <u>11/01/24 (1)</u>

twist 2 .036

Span 2 81.660 Use P/O as per ASTM 1417 level 2 as per QSI088

P/O: 13362 C211/011 2ce (1)

rec'd & inspect & attached c/c to w/o

10/01/26

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries



**Work Order ID 61768**

Thursday, September 02, 2010 11:28:13 AM

Page 5

Item ID: D350-748-201

Accept

Revision ID:

Item Name: Crosstube Installation, High Aft






Start Date: 9/2/2010 Start Qty: 1.00

Required Date: 9/20/2010 Req'd Qty: 1.00

Reference:

Approvals: Process Plan: \_\_\_\_\_ Date: \_\_\_\_\_ Tooling: \_\_\_\_\_ Date: \_\_\_\_\_  
QC: \_\_\_\_\_ Date: \_\_\_\_\_ SPC (Y/N): \_\_\_\_\_ Date: \_\_\_\_\_

Run Start  
Stop

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
180  SprayPaint Spray Painting	SprayPaint  Memo 1-Prime inside crosstube as per QSI 005 4.2 2-Paint Outside of Tube as per Dart QSI 005 4.2	0.00  0.00					11	01	31 (1)
190  QC Quality Control	QC14- Inspect Spray Paint  Memo Then, Wrap in plastic bag to protect from scratches	0.00  0.00					BT	11-02-02	
200  Crosstubes Crosstubes	Crosstubes  Memo 1-Install Ground wire Insert, then insert screw and washer 2-Install Abraison strips as per Dwg D350-748-241 & QSI 035. 3-Install supports Using Dt8876 as per Dwg D350-748-241, Torque to 60-80 IN-LBS	0.00  0.00					11	02	02 (1)

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

**Work Order ID 61768**

Thursday, September 02, 2010 11:28:13 AM



Page 6

Item ID: D350-748-201

Accept



Setup Start



Revision ID:

Stop



Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010 Start Qty: 1.00



Cust Item ID:

Required Date: 9/20/2010 Req'd Qty: 1.00

Customer:

Reference:

Approvals: Process Plan: \_\_\_\_\_ Date: \_\_\_\_\_ Tooling: \_\_\_\_\_ Date: \_\_\_\_\_

Run Start



QC: \_\_\_\_\_ Date: \_\_\_\_\_ SPC (Y/N): \_\_\_\_\_ Date: \_\_\_\_\_

Stop

Sequence ID/  
Work Center IDOperation  
DescriptionSet Up/  
Run Hours

Tool ID

Tool #

Plan  
CodeAccept  
QtyReject  
QtyReject  
NumberInsp.  
Stamp

210

QC5- Inspect part completeness to step on W/O

0.00



QC

Memo

0.00

Quality Control

8/11/02/02

⑦

220

Pick Kit

0.00



Packaging

Memo

0.00

Packaging

11/2/02/03

230

QC4- 100% Inspect kits for completeness

0.00



QC

Memo

0.00

Quality Control

8/11/02/03

⑦

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

**Work Order ID 61768**

Thursday, September 02, 2010 11:28:13 AM

Page 7

Item ID: D350-748-201

Accept

Setup Start

Revision ID:

Stop

Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010 Start Qty: 1.00

Cust Item ID:

Required Date: 9/20/2010 Req'd Qty: 1.00

Customer:

Reference:

Approvals: Process Plan: \_\_\_\_\_ Date: \_\_\_\_\_ Tooling: \_\_\_\_\_ Date: \_\_\_\_\_

Run Start

QC: \_\_\_\_\_ Date: \_\_\_\_\_ SPC (Y/N): \_\_\_\_\_ Date: \_\_\_\_\_

Stop

Sequence ID/  
Work Center IDOperation  
DescriptionSet Up/  
Run Hours

Tool ID

Tool #

Plan  
CodeAccept  
QtyReject  
QtyReject  
NumberInsp.  
Stamp

240

0.00



Packaging

Packaging

Memo

0.00

Packaging

Identify and pack for shipping as per PPPD350-748-201

Location: 102

PPP Rev: A

11/2/38

250

0.00



QC

QC21- Final Inspection - Work Order Release

Memo

0.00

Quality Control

11/02/04

MF  
11-02-03

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

# Picklist Print

Thursday, September 02, 2010 11:28:18 AM

Page 1

Work Order ID: 61768

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft


Start Date: 9/2/2010

Required Date: 9/20/2010

Start Qty: 1.00


Required Qty: 1.00

Comments: IPP Rev: A New Issue 06-07-05 JLM  
 IPP Rev: B Update qty of MS21042L5 06-09-12 KJ  
 IPP Rev C Combined manufacturing 08.04.02 EC verified by: DD  
 IPP Rev:D 08-06-24 revD as per dwg DD verified by:EC  
 IPP Rev: E 08.12.11 Step17 was step 21 KJ Verified by:EC IPP Rev:F  
 10.08.04 added QSI010 4.3 DD verf:EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D350-748-241TRN 		Manufactured	No			110	Each	3.0000	1	1			
Crosstube Turning Detail													


Location	Loc Qty	Loc Code
LG	3	
59549	1	
59551	1	
59587	1	

DP 10-12-7

ALS4-1032-225 		Purchased	No			200	Each	5,336.000	1	1			
Insert													

Location	Loc Qty	Loc Code
PK011	5336	
110768	5336	

11.02.02

AN960JD10 	NAS1149D0363J	Purchased	No			200	Each	6.0000	1	1			
Washer													

Location	Loc Qty	Loc Code
ST	6	
107715	6	

11.02.02

B# 116025

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries



# Picklist Print

Thursday, September 02, 2010 11:28:18 AM

Page 2

Work Order ID: 61768

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010

Required Date: 9/20/2010

Start Qty: 1.00

Required Qty: 1.00

D2856-400

Manufactured

No

200

f

313.4060

1.181

1.243158



Abraison Strip

13# 63735

Location

Loc Qty

Loc Code

ST403

313.4060421

56626

97.4060421

59920

216

1- cut as per dwg D2856

D3502-1

Manufactured

No

200

Each

54.0000

2

2



Support

Location

Loc Qty

Loc Code

ST063

12

61206

12

ST066

42

50287

38

52903

4

MS21920-20

Purchased

No

200

Each

77.0000

2

2



Clamp (per MIL-DTL-8783C)

Location

Loc Qty

Loc Code

LG

77

112624

6

114687

21

114779

24

115057

26

13# 115736

Thursday, September 02, 2010 11:28:18 AM

Shop Packet Print

Page 2

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

# Picklist Print

Thursday, September 02, 2010 11:28:18 AM

Page 3

Work Order ID: 61768

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010

Required Date: 9/20/2010

Start Qty: 1.00

Required Qty: 1.00

MS27039-1-10

Purchased

No

200

Each

126.0000

1

1



Screw



11.02.02

## Location

## Loc Qty

## Loc Code

ST291

126

112794

26

112940

100

AN4-41A

Purchased

No

220

Each

274.0000

8

8



Bolt



11/2/35

## Location

## Loc Qty

## Loc Code

ST337

40

ST360

234

111424

4

113359

30

114941

100

115108

100

AN4-6A

Purchased

No

220

Each

1,418.000

16

16



Bolt



11/2/35

## Location

## Loc Qty

## Loc Code

ST356

1418

112933

96

113149

19

114523

2

114615

1

114941

500

115108

300

115457

500

16

Thursday, September 02, 2010 11:28:18 AM

Shop Packet Print

Page 3

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

# Picklist Print

Thursday, September 02, 2010 11:28:18 AM

Page 4

Work Order ID: 61768

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010

Required Date: 9/20/2010

Start Qty: 1.00

Required Qty: 1.00

AN5-32A Purchased No

220 Each

196.0000

4

4



Bolt



M115698 11/2/3P

## Location

## Loc Qty

## Loc Code

ST340

196

113121

4

114056

42

114405

50

115016

50

115108

50

AN960JD416 NAS1149D0463J Purchased No

220 Each

0.0000

32

32



Washer



M116304 11/2/3P

AN960JD516 NAS1149D0563J Purchased No

220 Each

34.0000

8

8



Washer



M114742 11/2/3P

## Location

## Loc Qty

## Loc Code

ST

34

103694

18

107534

12

109287

4

D3500-1 Manufactured No

220 Each

30.0000

4

4



Saddle



M1163995 11/2/3P

## Location

## Loc Qty

## Loc Code

ST424

30

55605

2

59422

16

60489

12

Thursday, September 02, 2010 11:28:18 AM

Shop Packet Print

Page 4

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

# Picklist Print

Thursday, September 02, 2010 11:28:18 AM

Page 5

Work Order ID: 61768

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 9/2/2010

Required Date: 9/20/2010

Start Qty: 1.00

Required Qty: 1.00

D3501-1

Manufactured No

220

Each

394.0000

16

16



Bushing



11/8/38

Location

Loc Qty

Loc Code

ST066

394

45402

15

45918

112

48268

67

53779

100

61196

100

MS21042L4

Purchased No

220

Each

2,363.0000

24

24



Nut



11/6/38 11/2/38

Location

Loc Qty

Loc Code

ST300

2363

113422

68

114523

28

114718

16

114784

331

115108

1920

MS21042L5

Purchased No

220

Each

633.0000

4

4



Nut



11/5/38 11/2/38

Location

Loc Qty

Loc Code

ST139

133

114813

133

ST300

500

115156

500

Thursday, September 02, 2010 11:28:18 AM

Shop Packet Print

Page 5

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_


NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries



<b>DART AEROSPACE LTD</b>		<b>Work Order:</b>	41768
<b>Description:</b> Crosstube High Aft (AS350/355)		<b>Part Number:</b>	D350-748-201
<b>Inspection Dwg:</b> D350-748-241 <b>Rev:</b> E		<b>Page 1 of 1</b>	

Required Dimension	Min	Max
Height	31.22	31.48
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06

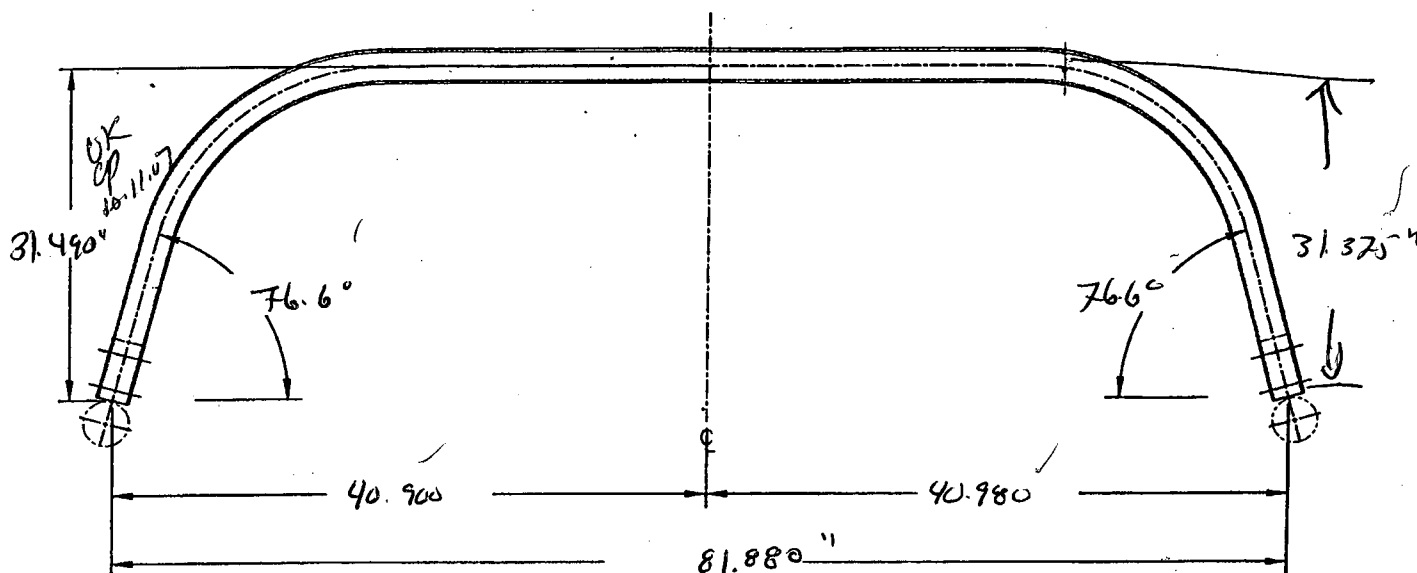

Comments
first 2 0.152" OK 10.11.07

QC15 Inspection	S
Date	10/12/07

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_


Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DART AEROSPACE LTD		Work Order:	
Description: Crosstube High Aft (AS350/355)		Part Number:	D350-748-201
Inspection Dwg: D350-748-241 Rev: E		Page 1 of 1	

Required Dimension	Min	Max
Height	31.22	31.48
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06

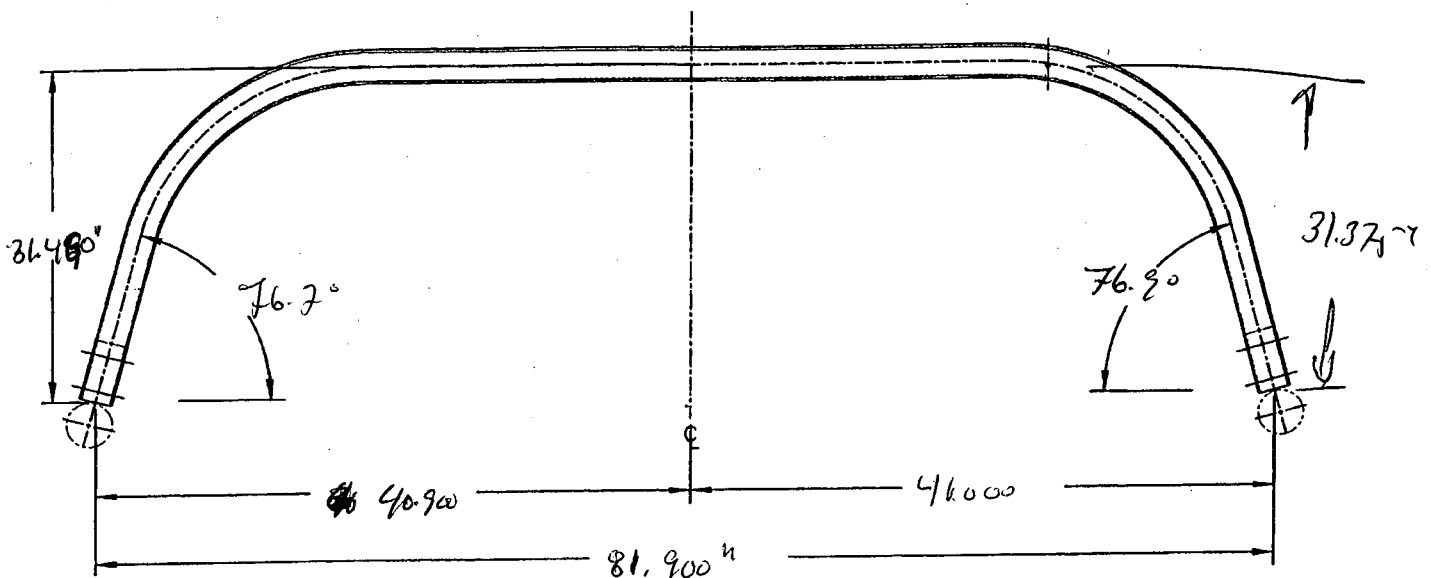

After stress relief


Comments
twist = 0.165 0.142"

QC15 Inspection	8
Date	10/12/06

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	

<b>DART AEROSPACE LTD</b>		<b>Work Order:</b>	
<b>Description:</b> Crosstube High Aft (AS350/355)		<b>Part Number:</b>	<b>D350-748-201</b>
<b>Inspection Dwg:</b> D350-748-241 <b>Rev:</b> E			<b>Page 1 of 1</b>

Required Dimension	Min	Max
Height	31.22	31.48
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06

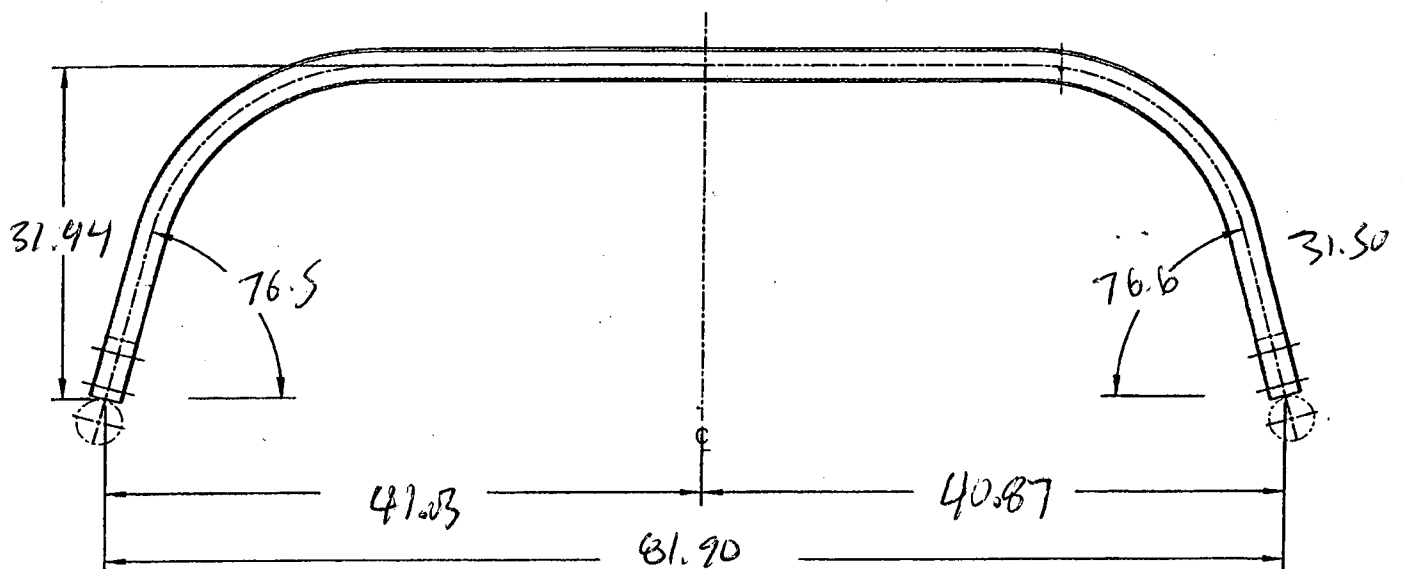

Comments
AFTER DEFLECTION TEST

QC15 Inspection	<i>[Signature]</i>
Date	10.12.22

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	<i>[Signature]</i>

Item	Qty -241	Part Number	Description
1	X	D350-748-241	CROSSTUBE ASSEMBLY (AS 350/355 HI AFT)
2	1	D6018-125	CROSSTUBE
3	2	D3502-1	SUPPORT
4	2	D2856-400-710	ABRASION STRIP
5	1	AELS-1032-225	INSERT
6	1	NAS1149D0363J	WASHER (OR AN960JD10)
7	2	MS21920-20	CLAMP (PER DART SPEC. M-MS21920-20)
8	1	MS27039-1-10	SCREW

# **GENERAL NOTES:**

- 1) MATERIAL: MANUFACTURED FROM D6018-125  
FINISHED LENGTH = 122.700±0.06
- 2) FINISH: MAGNETIC PARTICLE INSPECT PER DART QSI 038 4.2  
CADMIUM PLATE PER AMS-QQ-P-416B, CLASS 1, TYPE II  
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2  
PAINT OUTSIDE PER DART QSI 005 4.2
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED.
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX.
- 6) IDENTIFICATION: SCRIBE DART PART NUMBER "D350-748-241" AND BATCH NUMBER ON INSIDE OF CUFF USING VIBRATING STYLUS.
- 7) WEIGHT: 29.85 lbs
- 8) PART IS SYMMETRIC ABOUT CENTERLINE, EXCEPT FOR Ø0.297 HOLE.
- 9) RUN CUTTER OFF PART WHERE INDICATED. BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- 10) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 11) HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS 2759-1C AFTER TURNING.
- 12) INSTALL D2856-400-710 ABRASION STRIPS WITH A GAP ON BOTTOM SIDE OF CROSSTUBE, CENTERED OPPOSITE D3502-1 SUPPORT, PER QSI 035.
- 13) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.
- 14) TORQUE CLAMPS 60 TO 80 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING.

SHOP COPY  
RETURN TO  
ENGINEERING  
UNCONTROLLED COPY  
SUBJECT TO AMENDMENT  
WITHOUT NOTICE  
WORK ORDER

NO.

*2061748*

**RELEASED**  
2009-10-29

*10-9-08*

E	REVISE GENERAL NOTES; UPDATE TO CURRENT STANDARDS; RELOCATED FLAG #6 PER PAR 08-046 (ZN A8-3); ADD TOLERANCES (ZN C6-3, D2-3)	RF	09.09.30
D	MAG. PARTICLE AND CAD PLATE AS MFD.	CP	06.10.31
C	ADD CAD PLATING	CP	06.08.14
B	ADD D6018-125 & PRIME AND PAINT	CP	06.06.30
A	NEW ISSUE	CP	06.03.31
REV.	DESCRIPTION	BY	DATE
DESIGN	<i>RF</i>	<b>DART AEROSPACE LTD</b> HAWKESBURY, ONTARIO, CANADA	
DRAWN	RF		
CHECKED	<i>RF</i>	DRAWING NO.	REV. E
MFG. APPR.	<i>RF</i>	D350-748-241	SHEET 1 OF 4
APPROVED	<i>RF</i>	TITLE	SCALE
DE APPR.	<i>RF</i>	CROSSTUBE (AS 350/355 HI AFT)	NTS
DATE	09.09.30	COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	


W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

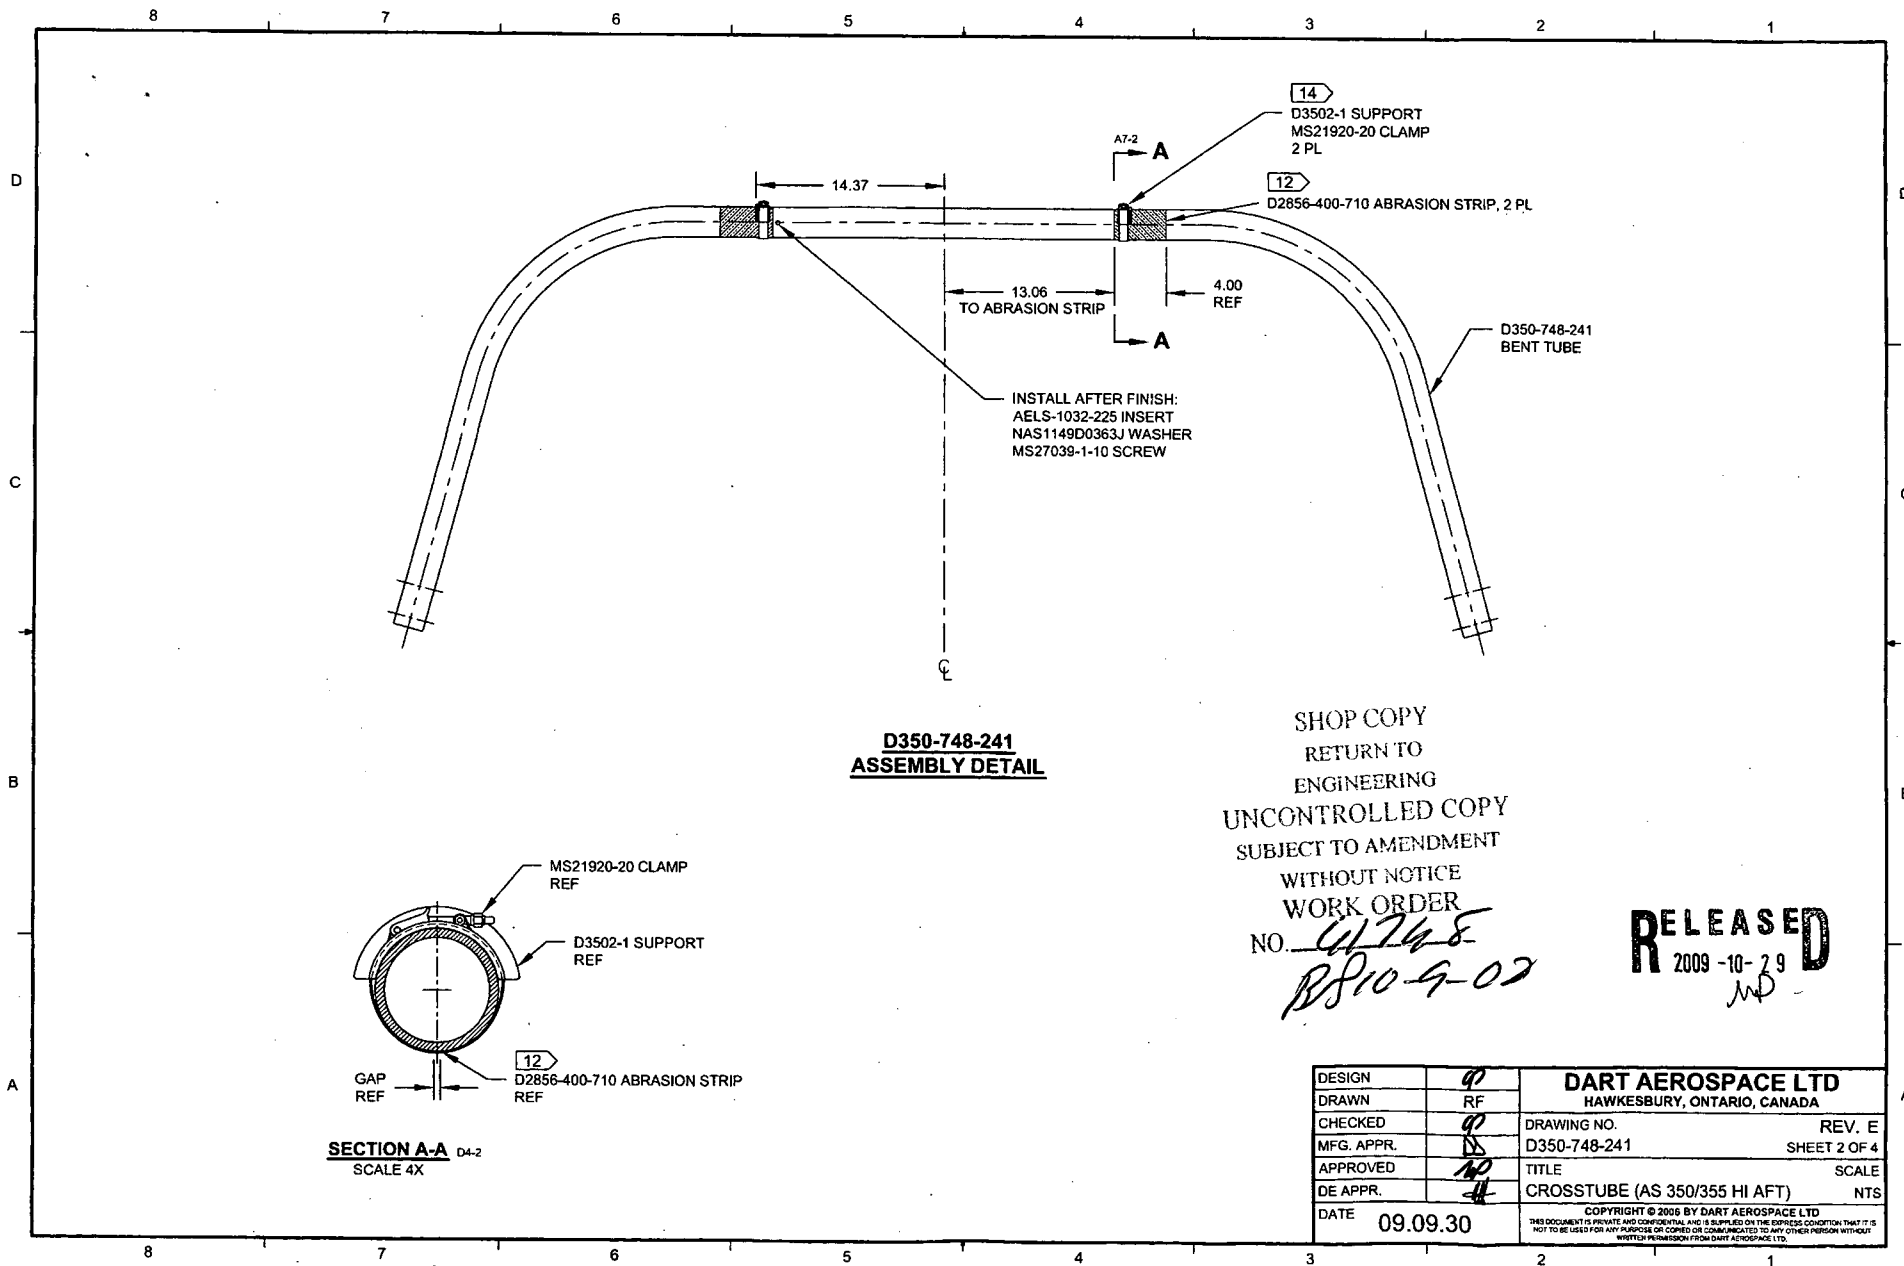

SHOP COPY  
RETURN TO  
ENGINEERING  
UNCONTROLLED COPY  
SUBJECT TO AMENDMENT  
WITHOUT NOTICE  
WORK ORDER  
NO. *41748*  
*BS10-9-02*

**RELEASED**  
2009-10-29  
*MB*

DESIGN	<i>9P</i>	<b>DART AEROSPACE LTD</b>	
DRAWN	RF	HAWKESBURY, ONTARIO, CANADA	
CHECKED	<i>9P</i>	DRAWING NO.	REV. E
MFG. APPR.	<i>DS</i>	D350-748-241	SHEET 2 OF 4
APPROVED	<i>10</i>	TITLE	SCALE
DE APPR.	<i>11</i>	CROSSTUBE (AS 350/355 HI AFT)	NTS
DATE	09.09.30	<small>COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.</small>	

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries






W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries

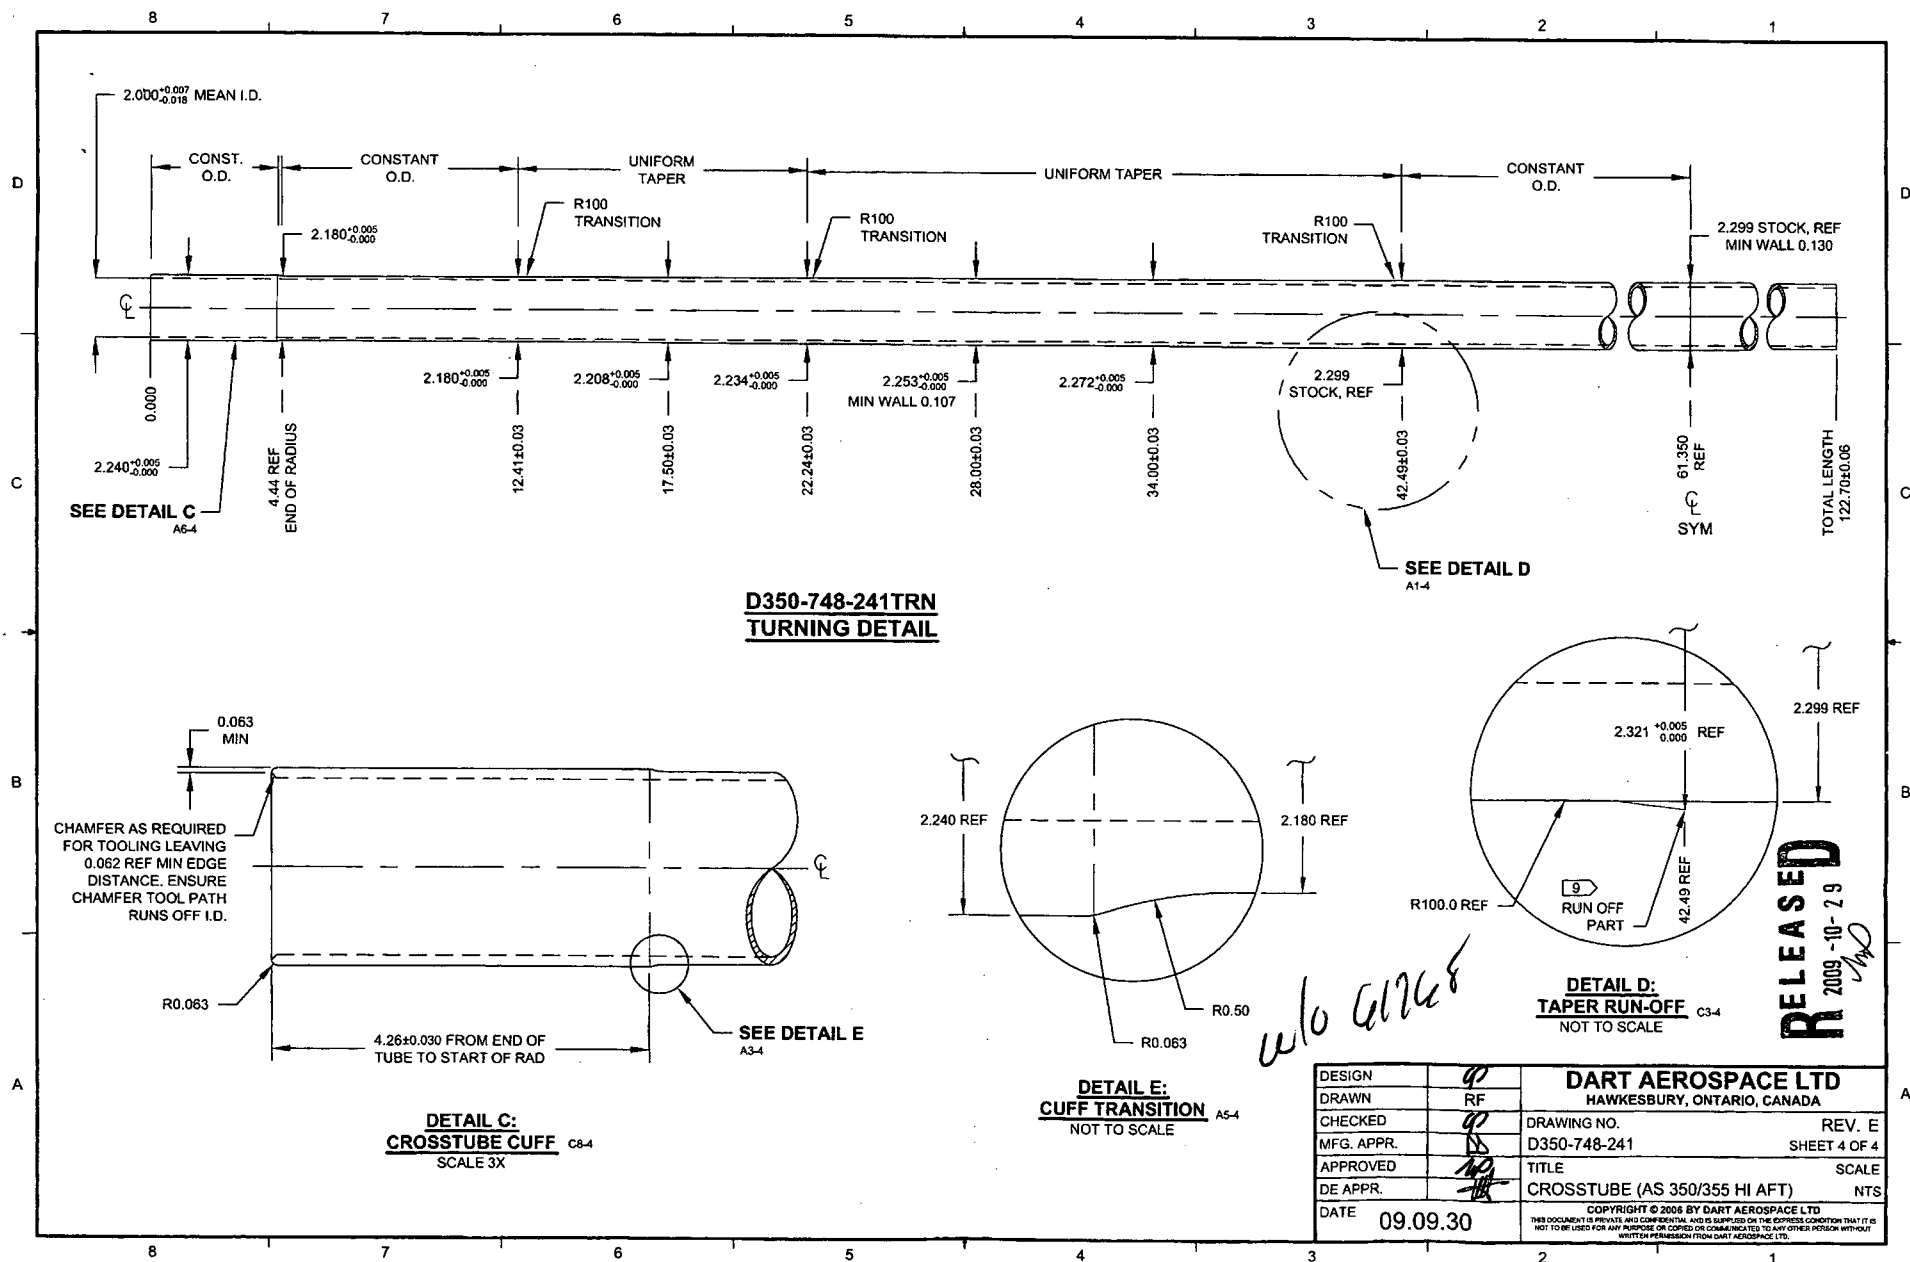

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

**NOTE:** Date & initial all entries



# LIQUID PENETRANT TEST REPORT

P- 15199

PAGE 1 OF 1

CLIENT DART AEROSPACE DATE DEC. 21-2010 TIME AM ☒ PM ☐  
ATTENTION LINDA LACELLE ACUREN JOB NO. 188-10-0971  
ADDRESS 1270 ABERDEEN ST. PO/WO NO. 13181  
HAWKESBURY ONT. WORK LOCATION HAWKESBURY PLANT  
ACCEPTANCE STD. ASTM 1417 REV./DATE 2005  
PROJECT SIX CROSS TUBES INSPECT + REINSPECT  
ITEM(S) EXAMINED AFTER DEFLECTION PROCESS.

JOB DESCRIPTION PROCEDURE NO. LT-002 REV./DATE 2008 TECHNIQUE NO. LT-002 REV./DATE 2008  
PART NO. - MATERIAL STEEL THICKNESS VARIOUS  
SCOPE WET FLUORESCENT LIQUID PENETRANT INSPECTION  
CARRIED OUT 100% EXTERNAL

## TEST DETAILS

METHOD ☒ FLUORESCENT ☐ VISIBLE ☒ WATER WASH ☐ SOLVENT REMOVABLE ☐ POST EMULSIFIED  
FAMILY BRAND MAGNA FLUX BLACK LIGHT S/N 16459 ☐ OUTPUT > 1000  $\mu$ W/cm<sup>2</sup> ☐ AMBIENT < 2 fc  
PENETRANT ZL67 MINIMUM DWELL TIME 45 MIN. LIGHTING EQUIP. ☐ FLASHLIGHT ☐ TROUBLELIGHT ☐ OUTPUT > 100 fc @ SURFACE  
PENETRANT REMOVER H2O MINIMUM DRY TIME >10 MIN. OTHER LABINO  
DEVELOPER SKD52 MINIMUM DWELL TIME 10 MIN. LIGHT METER S/N 1098866 CAL DUE DATE 02-19-2011  
DEVELOPER TYPE ☒ NON AQUEOUS ☐ AQUEOUS ☐ DRY

## TEST SURFACE

SURFACE CONDITION ☐ AS GROUND ☐ AS WELDED ☒ MACHINED ☐ SHOT BLASTED ☒ CLEAN BARE METAL  
SURFACE TEMPERATURE ☐ < -4°C/ 20°F ☐ -4°C/ 20°F TO 10°C/ 50°F ☒ 10°C/ 50°F TO 52°C/ 125°F ☐ > 52°C/ 125°F

## RESULTS- ( ☐ METRIC ☐ IMPERIAL )

REINSPECT

1 - CROSS TUBE-W.O. 61768	✓
1 - CROSS TUBE-W.O. 61767	✓
1 - CROSS TUBE-W.O. 61770	✓
1 - CROSS TUBE-W.O. 61769	✓
1 - CROSS TUBE-W.O. 63592	✓
1 - CROSS TUBE-W.O. 63591	✓
1 - CROSS TUBE-W.O. 61768	✓
1 - CROSS TUBE-W.O. 61767	✓
1 - CROSS TUBE-W.O. 61770	✓
1 - CROSS TUBE-W.O. 61769	✓
1 - CROSS TUBE-W.O. 63592	✓
1 - CROSS TUBE-W.O. 63591	✓

Cross Tubes REINSPECTED AFTER DEFLECTION RESULTS AS FOLLOWS.

10.12.21

**Scope of Services**  
The agreement of Acuren Group Inc. to perform services extends only to those services provided for in writing. Under no circumstances shall such services extend beyond the performance of the requested services. It is expressly understood that all descriptions, comments and expressions of opinion reflect the opinions or observations of Acuren Group Inc. based on information and assumptions supplied by the owner/operator and are not intended nor can they be construed as representations or warranties. Acuren Group Inc. is not assuming any responsibilities of the owner/operator and the owner/operator retains complete responsibility for the engineering, manufacture, repair and use decisions as a result of the data or other information provided by Acuren Group Inc. In no event shall Acuren Group Inc.'s liability in respect of the services referred to herein exceed the amount paid for such services.

**Standard of Care**  
In performing the services provided, Acuren Group Inc. uses the degree, care and skill ordinarily exercised under similar circumstances by others performing such services in the same or similar locality. No other warranty, expressed or implied, is made or intended by Acuren Group Inc.

## SIGNATURES

CLIENT REPRESENTATIVE R. Titley DTR # E63236  
TECHNICIAN (SIGNATURE): [Signature] REPORT REVIEWED BY:  
NAME (PRINT): Mike Johnston NAME INITIALS  
1<sup>ST</sup> TECHNICIAN 2<sup>ND</sup> TECHNICIAN  
CGSB LEVEL 2 SNT LEVEL \_\_\_\_\_ CGSB LEVEL \_\_\_\_\_ SNT LEVEL \_\_\_\_\_  
CGSB REG. NO. 6606 CGSB REG. NO. \_\_\_\_\_

W/O:		WORK ORDER CHANGES						
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector	
10.12.21	140.5	- DEFLECT TUBE TO <u>3000</u> lbs FOR 1 MINUTE. - RE-MEASURE HEIGHT & WIDTH.	CP	10.12.21		CP 10.12.21 QS/012	S 10.12.22	
10.12.21	140.6	NDT Tube Following deflection testing.				CP 10.12.21 QS/012	S 10.12.22	

Part No: \_\_\_\_\_ PAR #: \_\_\_\_\_ Fault Category: \_\_\_\_\_ NCR: Yes No DQA: \_\_\_\_\_ Date: \_\_\_\_\_

Resolution: \_\_\_\_\_ Disposition: \_\_\_\_\_ QA: N/C Closed: \_\_\_\_\_ Date: \_\_\_\_\_

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

**CERTIFICATE OF  
CONFORMANCE**

**CADORATH PLATING CO. LTD.  
2150 LOGAN AVENUE  
WINNIPEG, MANITOBA R2J-0J1**

**DATE:** Jan-14-2011

**CONSIGNED TO:** Dart Aerospace Ltd.  
1270 Aberdeen St  
Hawksbury, ON K6A 1K7

**W/O #:** 101008

**INVOICE #:** 52908

**CONTRACT OR  
PURCHASE ORDER #** 13189

**DESCRIPTION:** SKID

**QTY** 1

**P/N #** D350-748-201

**S/N #** B61768

**STRESS RELIEF BAKE @375 DEG. BAKE HEAT CHART #11-5. MPI  
INSPECTED IAW ASTM-E-1444. CADMIUM PLATED IAW AMS-QQ-P-  
416C, TYPE 2 YELLOW, CLASS 1. BAKE HEAT CHART #11-24.**

*rubiky*

**CERTIFICATE: I certify that the items indicated here on have  
been inspected and tested and conform to all specifications  
and requirements detailed on the contract or purchase order.**

**Approved Inspector:**





## LIQUID PENETRANT TEST REPORT

P- 05496 :

CLIENT DART AEROSPACE DATE JAN/26/2011 PAGE 1 OF 2  
ATTENTION LINDA LACROIX / CHANTALE / IAN ACUREN JOB NO. 188-11- TIME AM ☒ PM ☐  
ADDRESS 1270, ABERDEN ST. POWO No. AS ADDRESS  
HAWKESBURY, ON WORK LOCATION AS ADDRESS  
ACCEPTANCE STD. ASTM1417/OST-038 REV./DATE 2005  
PROJECT WET FLUO PENETRANT INSPECTION ON 14 "CROSSTUBES"; 4 "collective BEEL CRACK"  
ITEM(S) EXAMINED SEE BELOW

JOB DESCRIPTION PROCEDURE NO. LT-002 REV./DATE 2008 TECHNIQUE No. LT-002 REV./DATE 2008  
PART NO. MATERIAL ALUMINUM ALLOY THICKNESS N/A  
SCOPE PERFORMED A WET FLUORESCENT LIQUID PENETRANT INSPECTION ON 100% OF THE EXTERNAL SURFACE

## TEST DETAILS

METHOD ☒ FLUORESCENT ☐ VISIBLE ☐ WATER WASH ☐ SOLVENT REMOVABLE ☐ POST EMULSIFIED  
FAMILY BRAND MAGNA FLUX BLACK LIGHT S/N 13798 ☒ OUTPUT > 1000  $\mu$ W/cm<sup>2</sup> ☐ AMBIENT < 2 fc  
PENETRANT 26-67 MINIMUM DWELL TIME 10 MIN. LIGHTING EQUIP. ☐ FLASHLIGHT ☐ TROUBLELIGHT ☐ OUTPUT > 100 fc @ SURFACE  
PENETRANT REMOVER H<sub>2</sub>O MINIMUM DRY TIME >10 MIN. OTHER  
DEVELOPER SKD-52 MINIMUM DWELL TIME 10 MIN. LIGHT METER S/N CAL DUE DATE FEB/25/2011  
DEVELOPER TYPE ☒ NON AQUEOUS ☐ AQUEOUS ☐ DRY

## TEST SURFACE

SURFACE CONDITION ☐ AS GROUND ☐ AS WELDED ☐ MACHINED ☐ SHOT BLASTED ☒ CLEAN BARE METAL  
SURFACE TEMPERATURE ☐ < -4°C/ 20°F ☐ -4°C/ 20°F TO 10°C/50°F ☒ 10°C/50°F TO 52°C/125°F ☐ > 52°C/125°F

RESULTS- ☐ METRIC ☒ IMPERIAL

ITEM NO.	DESCRIPTION	ACCEPTED	REJECTED
1	4 X "collective BEEL CRACK"	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2	CROSS-TUBE W.O. ID 63591	<input checked="" type="checkbox"/>	<input type="checkbox"/>
3	CROSS-TUBE W.O. ID 63592	<input checked="" type="checkbox"/>	<input type="checkbox"/>
4	CROSS-TUBE W.O. ID 63746	<input checked="" type="checkbox"/>	<input type="checkbox"/>
5	CROSS-TUBE W.O. ID 63747	<input checked="" type="checkbox"/>	<input type="checkbox"/>
6	CROSS-TUBE W.O. ID 63748	<input checked="" type="checkbox"/>	<input type="checkbox"/>
7	CROSS-TUBE W.O. ID 63749	<input checked="" type="checkbox"/>	<input type="checkbox"/>

SEE Page 2 of 2

W01D 64913 → ITEM ID: - D350-748-101 (H.F.)  
ITEM ID: - D350-748-101 (H.F.)  
ITEM ID: - D350-748-101 (H.F.)  
ITEM ID: - D350-748-201 (H.A.)  
ITEM ID: - D350-748-201 (H.A.)  
ITEM ID: - D350-748-201 (H.A.)  
ITEM ID: - D350-748-201 (H.A.)

1/21/2011

## Scope of Services

The agreement of Acuren Group Inc. to perform services extends only to those services provided for in writing. Under no circumstances shall such services extend beyond the performance of the requested services. It is expressly understood that all descriptions, comments and expressions of opinion reflect the opinions or observations of Acuren Group Inc. based on information and assumptions supplied by the owner/operator and are not intended nor can they be construed as representations or warranties. Acuren Group Inc. is not assuming any responsibilities of the owner/operator and the owner/operator retains complete responsibility for the engineering, manufacture, repair and use decisions as a result of the data or other information provided by Acuren Group Inc. In no event shall Acuren Group Inc.'s liability in respect of the services referred to herein exceed the amount paid for such services.

## Standard of Care

In performing the services provided, Acuren Group Inc. uses the degree, care and skill ordinarily exercised under similar circumstances by others performing such services in the same or similar locality. No other warranty, expressed or implied, is made or intended by Acuren Group Inc.

## SIGNATURES

CLIENT REPRESENTATIVE Jan T. Hay DTR # E63121  
TECHNICIAN (SIGNATURE): [Signature] SIGNATURE  
NAME (PRINT): VESDESPOSIERS REPORT REVIEWED BY: [Signature]  
CGSB LEVEL 2 SNT LEVEL 2 CGSB LEVEL 2 SNT LEVEL 2  
CGSB REG. NO. 3044 CGSB REG. NO. 3044





## RAPPORT D'INSPECTION NON DESTRUCTIVE

(SUITE)

REPORT# P-05496

PAGE 2 DE 2

CLIENT DART AEROSPACE  
ATTENTION LINDA LACELLE / CHARITAKE / IANDATE JAN/26/2011 HEURE ☒ AM ☐ PM  
ACUREN W/O : 188-11-02103RÉSULTATS ( ☐ MÉTRIQUE ☒ IMPÉRIALE )

ITEM	COMMENTS	ACCEPT	REJECT	ITEM ID
8	CROSS TUBE W.O. ID 61763	✓		ITEM ID: D350-748-101(H.F.)
9	CROSS TUBE W.O. ID 61764	✓		D350-748-101(H.F.)
10	CROSS TUBE W.O. ID 61765	✓		D350-748-101(H.F.)
11	CROSS TUBE W.O. ID 61766	✓		D350-748-101(H.F.)
12	CROSS TUBE W.O. ID 61767	✓		D350-748-201(H.A.)
13	CROSS TUBE W.O. ID 61768	✓		D350-748-201(H.A.)
14	CROSS TUBE W.O. ID 61769	✓		D350-748-201(H.A.)
15	CROSS TUBE W.O. ID 61770	✓		D350-748-201(H.A.)

— NO REJECTABLE INDICATION WAS DETECTED, AS PER APPLICABLE STANDARD

## Étendue des services

L'entente selon laquelle le Groupe Acuren Inc. exécute les services ne concerne que les énoncés par écrit. En aucune circonstance ces services ne s'étendent au-delà de l'exécution des services demandés. Il est entendu que toutes les descriptions, les observations et les expressions d'opinions faites par Acuren reflètent les opinions ou les observations de l'entreprise fondées sur l'information et les hypothèses fournies par le propriétaire/opérateur, et elles ne constituent pas des déclarations ou des garanties ou ne peuvent être interprétées comme constituant. Le groupe Acuren Inc. n'assume aucune des responsabilités du propriétaire/opérateur, et le propriétaire/opérateur conserve la responsabilité entière des décisions prises en matière d'ingénierie, de fabrication, de réparation et d'usage à partir de l'information ou des données fournies par Acuren en rapport avec les services décrits dans les présentes ne peuvent excéder le coût des services rendus.

## Norme de Diligence

Dans l'exécution des services, le Groupe Acuren inc. applique le degré de diligence, le soin et la compétence normalement exercés dans des circonstances semblables par d'autres fournisseurs de ce type de services opérant dans la même localité ou dans une localité similaire. Aucune autre garantie, implicite ou explicite, n'est faite ou voulue par le Groupe Acuren Inc.

## SIGNATURES

REPRÉSENTANT CLIENT

TECHNICIEN (SIGNATURE):

NOM (MOULIÉ):

Ian Titley MOULÉ  
J. DESJARDIS SIGNATURE  
1<sup>ER</sup> TECHNICIEN 2<sup>ME</sup> TECHNICIEN  
ONGC NIVEAU 2 SNT NIVEAU 2 ONGC NIVEAU — SNT NIVEAU —  
ONGC N° REGISTRATION 3049 ONGC N° REGISTRATION —

FTJ#: E63121

RAPPORT

RÉVISÉ PAR:

NOM

INITIALES
